


# 2021 Bond Update



**Presented By:  
ESC Region 13 and Sledge Engineering**

Board Meeting  
June 19, 2024

# Overall Bond Project Status– Current as of 06/12/24

Project	Design	Bid	Construct	Open	
Athletics Turf Baseball/Softball				Jan-22	
Safety/Security–Cameras HS&MS				Jan-22	
Safety/Security–Cameras JES&IES				Feb-23	
HS Parking Lot & Transportation				Dec-22	
HS Athletics Improvements				Apr-23	
HS Stormwater				Dec-22	
Double Creek Elem School			* Punch List *	Aug-23	
Middle School Expansion			* Punch List *	Aug-23	
1916 Building Renovations			99%	Jun-24	11/23/23
High School Expansion			86%	Aug-24	06/08/24
Transportation Expansion				Dec-23	
Technology Infrastructure				Dec-23	


# Summary Status of Construction Projects:

## 1. DCES & JMS

- a) Addressing punch list items (*DEADLINE to complete all work is 7/31/24*)
- b) Finalizing closeout documentation
- c) DCES Retainage = **\$1.7 million**
- d) JMS Retainage = **\$905k**

## 2. 1916


1. Addressing punch list items (*Elevator State Inspection is final item!*)
2. Technology “complete”
3. Furniture install “complete”
4. Billed to Date = **96%**
5. Retainage Balance to Pay = **\$540,000**

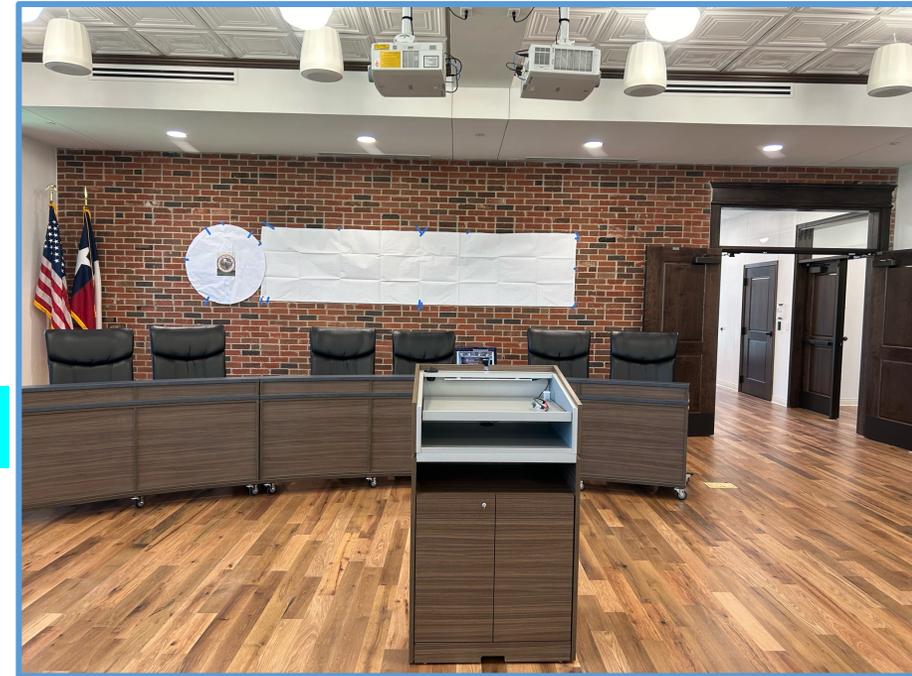


# Summary Status of Construction Projects (*continued*):

## 3. JHS Additions and Renovations

- a) Kitchen – Equipment install continues
- b) Classroom & Band Hall – Finishes continue
- c) Completion Date = **07/16/24** (*Original date 06/08/24*)
- d) Percent “Complete” = **86%** as of **05/31/24**
- e) Balance to Pay = **\$5 million**

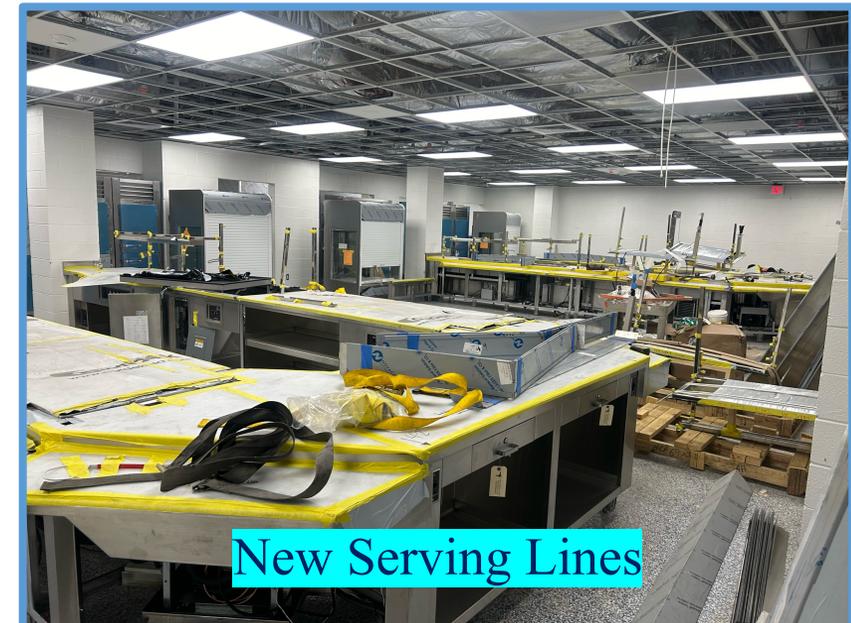

# Project Accounting – Summary (06/12/24)

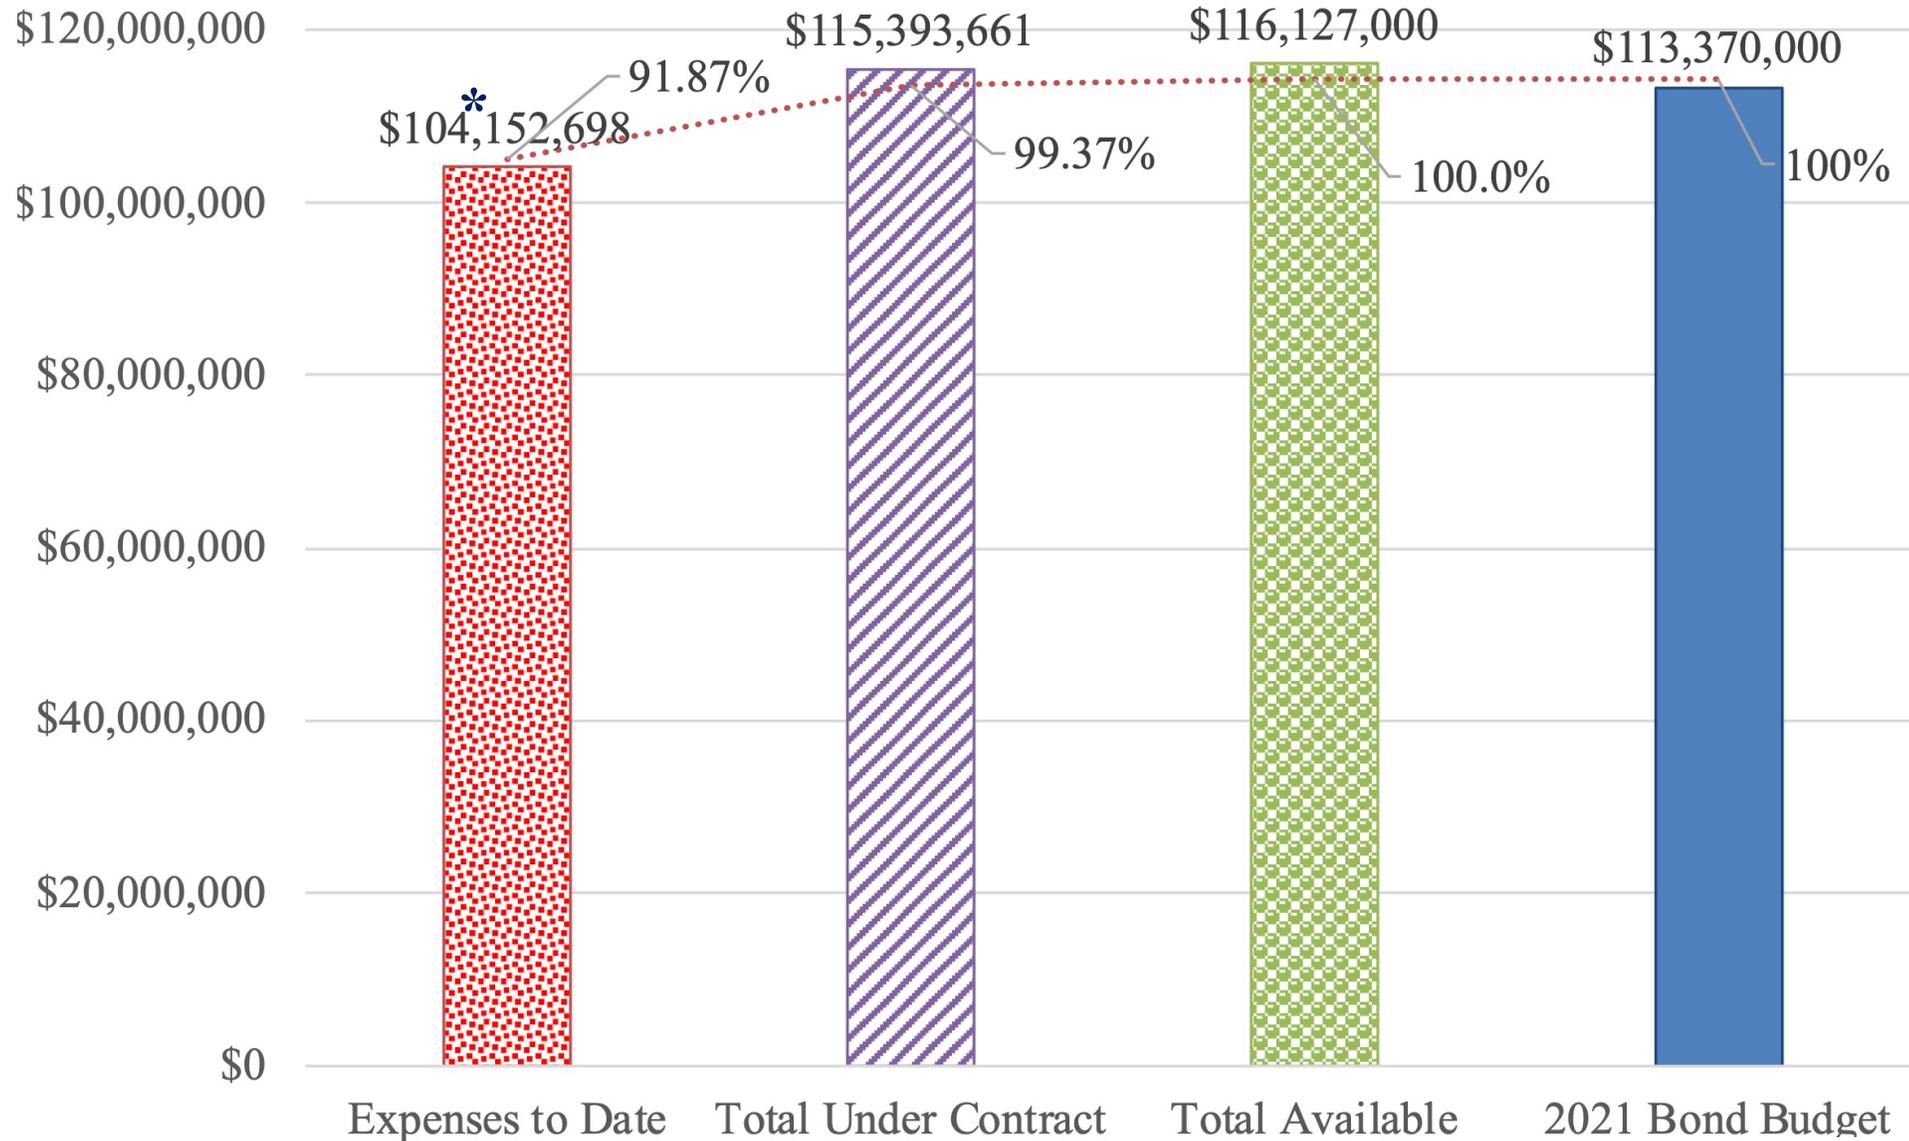

\* Previous Report = \$102.6 million

■ Amount    ..... Percent



*Any  
Questions?*



**Jarrell  
Independent School District**



**REGION 13**  
EDUCATION SERVICE CENTER

